DELAWARE COUNTY ROAD IMPROVEMENT PROGRAM - 2009

ID	Task Name	Material	QTY	Duration	Start	Finish	Predecessors
1	**KCC# 14760 - 2009 Delaware County Road Imprvt Prgm (9/4/09)**			**74 days**	**Tue 5/26/09**	**Fri 9/4/09**	
2	**Pavement Repair**		**5,600 TN**	**51 days**	**Tue 5/26/09**	**Tue 8/4/09**	
3	Ostrander (6" Repairs)	301	510 TN	2 days	Tue 5/26/09	Wed 5/27/09	
4	Concord (Mill Butt Joints)	301	100 TN	1 day	Thu 5/28/09	Thu 5/28/09	3
5	Moore (Contingency - Unknown Qty)	301/404	210 TN?	1 day	Fri 5/29/09	Fri 5/29/09	4
6	Concord/Harriot (Contingency -.Unknown Qty)	301/404	234 TN?	1 day	Mon 6/1/09	Mon 6/1/09	5
7	Cook	301	20 TN	1 day	Mon 6/1/09	Mon 6/1/09	5SS
8	Home	301/404	210 TN?	1 day	Fri 6/5/09	Fri 6/5/09	30
9	Steitz	301	278 TN	1 day	Mon 6/8/09	Mon 6/8/09	8
10	****Sawmill Parkway Extension Asphalt Paving****			**9 days**	**Tue 6/9/09**	**Fri 6/19/09**	9
11	Liberty	301/404	210 TN?	1 day	Mon 6/22/09	Mon 6/22/09	10
12	Braumiller (Mill Butt Joints)	301	12 TN	1 day	Tue 6/23/09	Tue 6/23/09	11
13	East & West Orange	270		1 day	Thu 6/25/09	Thu 6/25/09	12
14	Sedona	301/404	78 TN	1 day	Fri 6/26/09	Fri 6/26/09	13
15	Bale Kenyon	301/404	358 TN	1 day	Mon 6/29/09	Mon 6/29/09	14
16	Africa	301/404	210 TN?	1 day	Tue 6/30/09	Tue 6/30/09	15
17	Tussic	301/404	210 TN?	1 day	Wed 7/1/09	Wed 7/1/09	16
18	North & South Galena (Mill Butt Joints)	301	678 TN	3 days	Thu 7/2/09	Mon 7/6/09	17
19	Stockwell & Wilson	301	256 TN	1 day	Tue 7/7/09	Tue 7/7/09	18
20	North Old State (Mill Butt Joints)	301	1156 TN	3 days	Tue 7/14/09	Thu 7/16/09	57
21	County Home (Contingency - Unknown Qty)	301/404	210 TN?	1 day	Tue 7/28/09	Tue 7/28/09	58
22	Steamtown (Contingency - Unknown Qty)	301/404	210 TN?	1 day	Wed 7/29/09	Wed 7/29/09	21
23	Briarcliff	301	30 TN	1 day	Tue 8/4/09	Tue 8/4/09	48SS
24	Brewster/Attucks	301	16 TN	1 day	Tue 8/4/09	Tue 8/4/09	23SS
25							
26	**Asphalt Paving /Structure Overlay/Speed Tables**			**64 days**	**Tue 6/2/09**	**Fri 8/28/09**	
27	Concord Rd.	402	668 TN	1 day	Tue 6/2/09	Tue 6/2/09	64
28	Delaware St.	402/404	33 TN/27 TN	1 day	Wed 6/3/09	Wed 6/3/09	27
29	Serenity Dr. (Mill Butt Joints)	404	75 TN	1 day	Wed 6/3/09	Wed 6/3/09	28SS
30	Braumiller	403/404	424 TN/509 TN	1 day	Thu 6/4/09	Thu 6/4/09	29
31	McGinnis	403/404	171 TN/205 TN	1 day	Thu 6/4/09	Thu 6/4/09	30SS
32	North & South Galena	402	2423 TN	2 days	Thu 7/9/09	Fri 7/10/09	72
33	North Old State	402	4840 TN	3 days	Tue 7/21/09	Thu 7/23/09	73
34	Harris (Pulverization)	402	1628 TN	2 days	Fri 7/24/09	Mon 7/27/09	33
35	Structural Overlay - Gorsuch	404/617	45 TN	1 day	Tue 7/28/09	Tue 7/28/09	34
36	Gorsuch	402	160 TN	1 day	Tue 7/28/09	Tue 7/28/09	35SS
37	Village of Center Village Roads	404	360 TN	1 day	Tue 7/28/09	Tue 7/28/09	35SS
38	Genoa Twp. (Various Roads)	404	9784 TN	10 days	Wed 7/29/09	Tue 8/11/09	37
39	Worthington	403/448-1H	467 TN/979 TN	1 day	Wed 8/12/09	Wed 8/12/09	38
40	Orange Twp. (Green Bower/Sloop/Payson/Village of Lewis Center)	404/448-1H	2429 TN	3 days	Thu 8/13/09	Mon 8/17/09	39
41	Liberty Twp. (Briarcliff/Brewster/Attucks)	402/404	612 TN/1018 TN	2 days	Tue 8/18/09	Wed 8/19/09	40
42	Speed Tables (Carriage Rd. & Wren Ln.) - Incl Detour & Table Signage	404	100 TN	5 days	Thu 8/20/09	Wed 8/26/09	41
43	Lane	402	3086 TN	2 days	Thu 8/27/09	Fri 8/28/09	42
44							
45	**Mill Schedule**		**93,077 SY**	**11 days**	**Wed 7/22/09**	**Wed 8/5/09**	
46	Genoa Twp. (Various Roads)		66,081 SY	7 days	Wed 7/22/09	Thu 7/30/09	
47	Orange Twp. (Green Bower/Sloop/Payson)		14,701 SY	2 days	Fri 7/31/09	Mon 8/3/09	46
48	Liberty Twp. (Briarcliff/Brewster/Attucks)		11,100 SY	2 days	Tue 8/4/09	Wed 8/5/09	47
49							
50	**304 Aggregate Base/Grading (Porter Twp)**		**4,685 TN**	**4 days**	**Fri 8/21/09**	**Wed 8/26/09**	
51	Lane Rd. (Place 304 Agg Base)		4,685 TN	2 days	Fri 8/21/09	Mon 8/24/09	
52	Lane Rd. (Fine Grade 304 Agg)		25,250 SY	2 days	Tue 8/25/09	Wed 8/26/09	51
53							
54	**617 Aggregate Berm**		**3,707 TN**	**64 days**	**Wed 6/3/09**	**Mon 8/31/09**	
55	Concord Rd.		115 TN	1 day	Wed 6/3/09	Wed 6/3/09	29SS
56	Cheshire West		127 TN	1 day	Thu 6/4/09	Thu 6/4/09	30SS

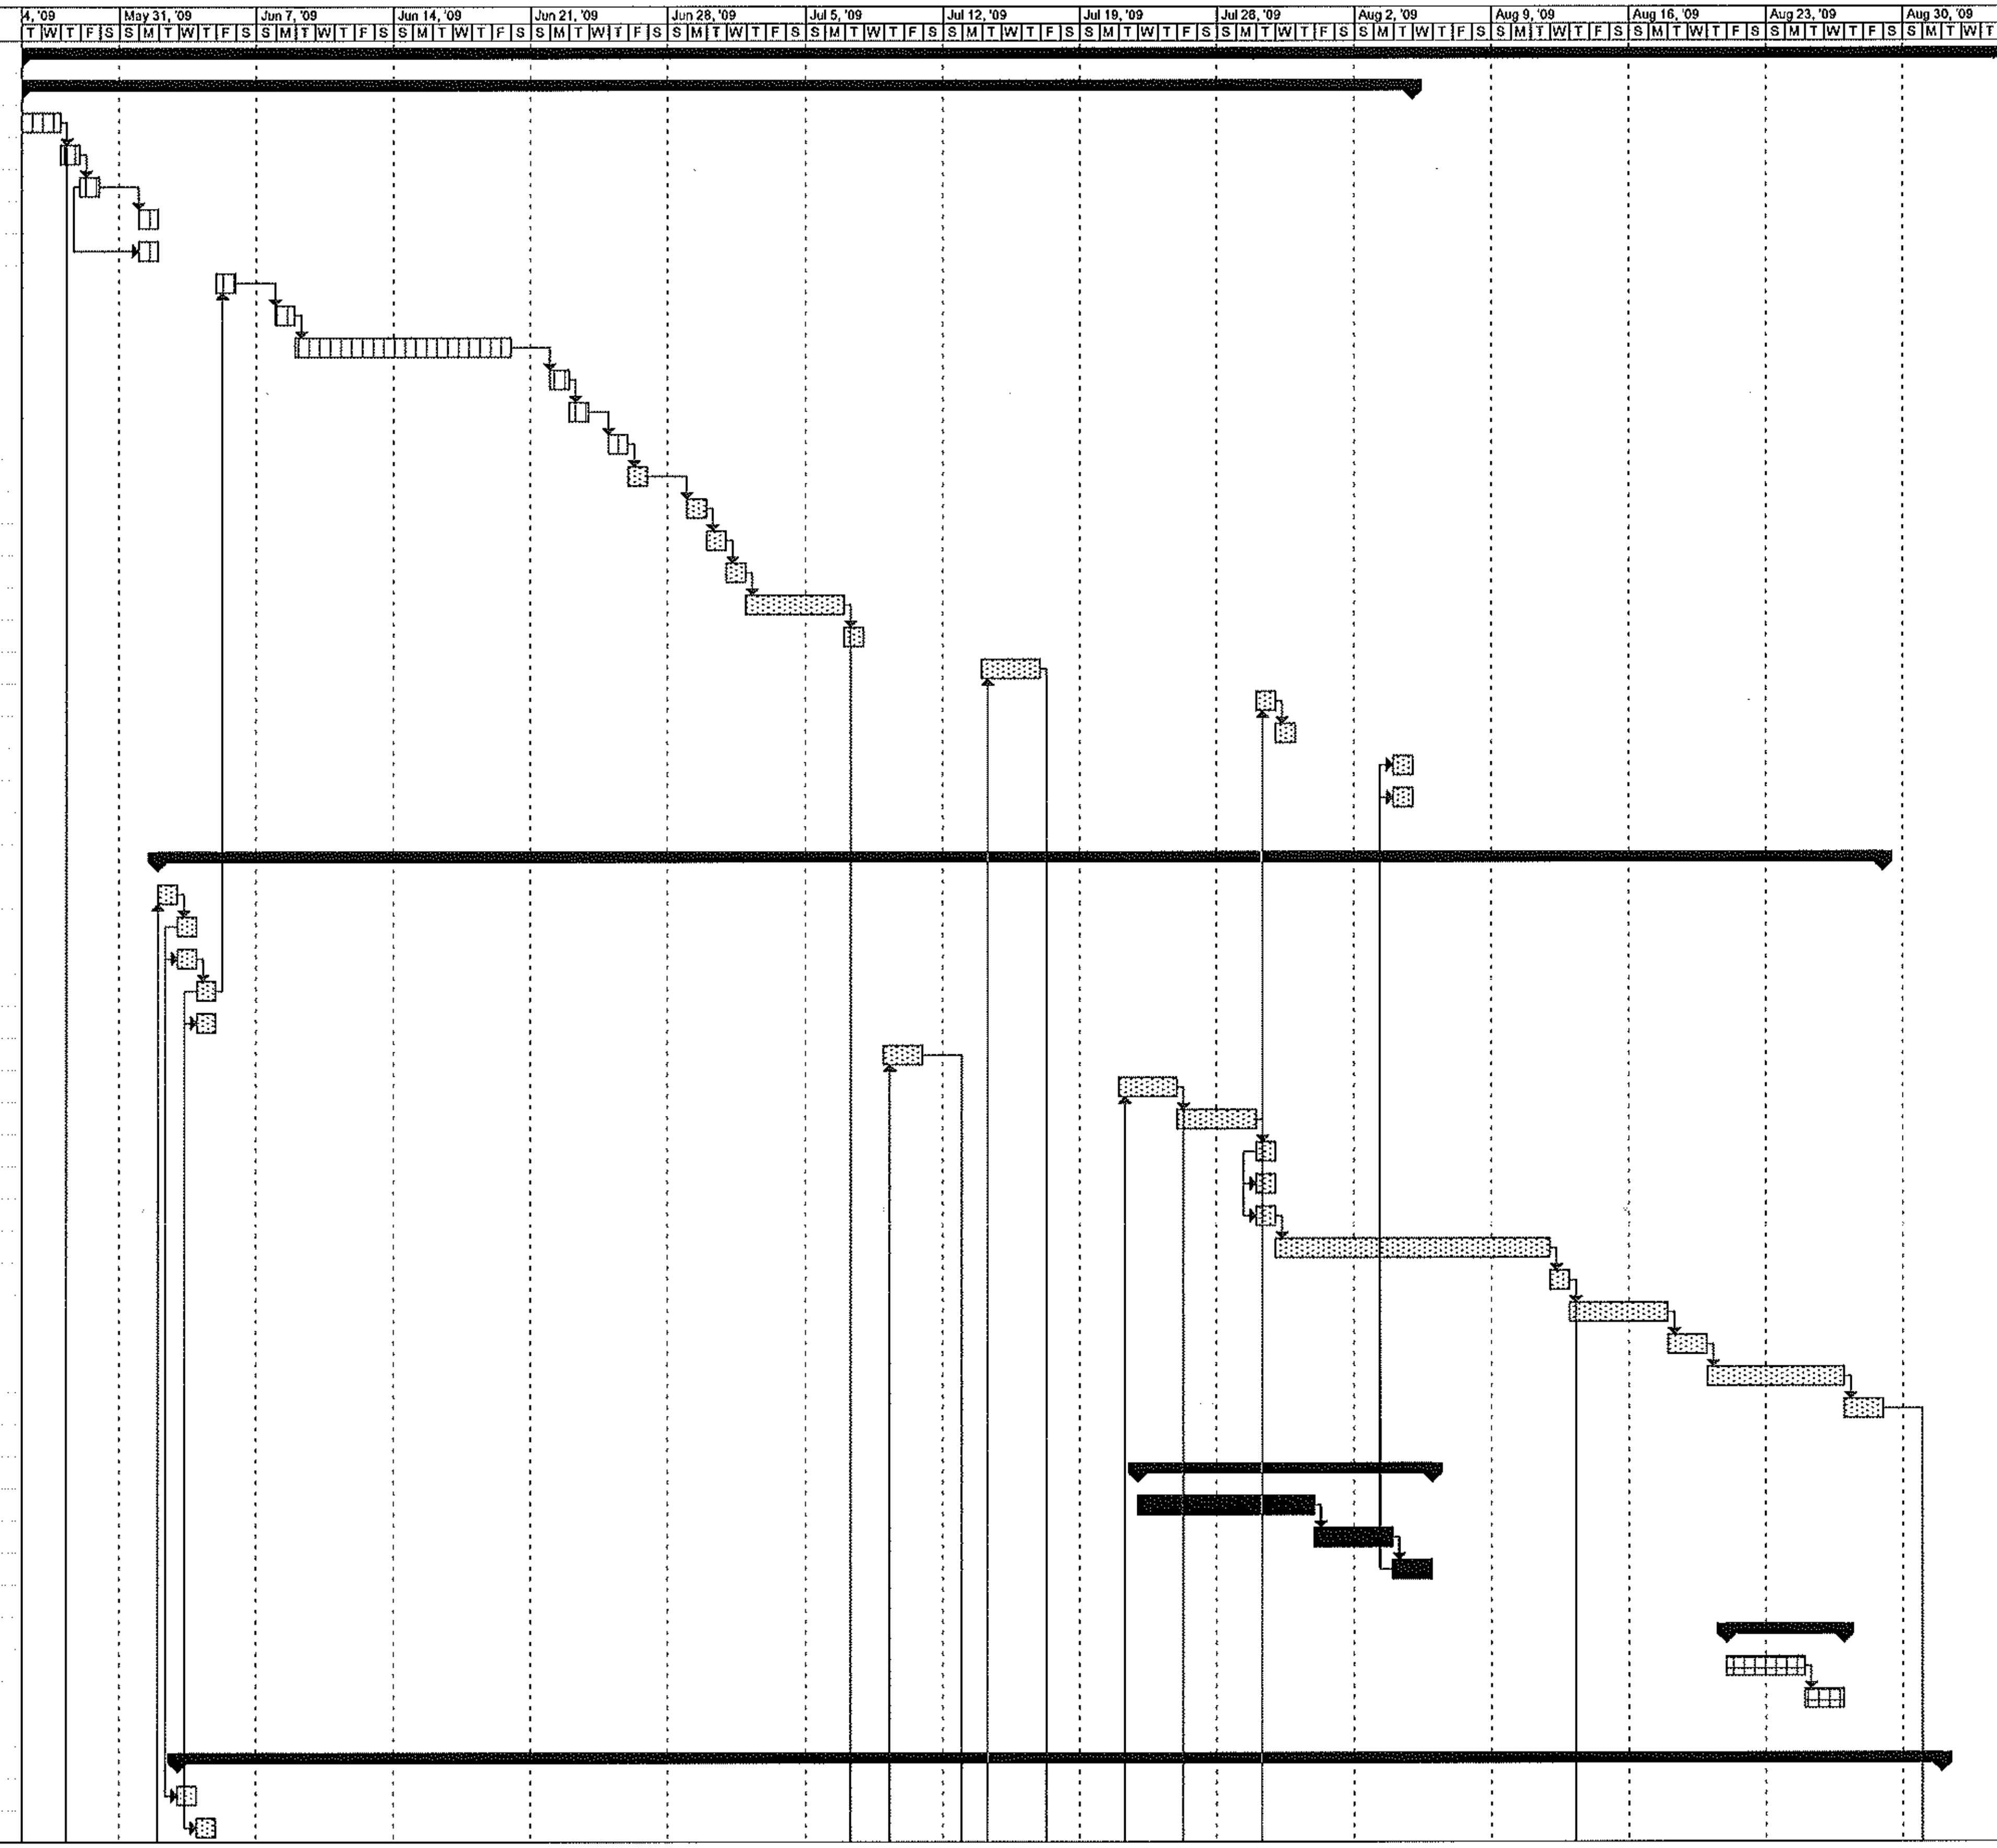

Project: Delaware Co
Date: Wed 5/20/09

Task | Progress | Summary | Rolled Up Split | Rolled Up Progress | Project Summary
Split | Milestone | Rolled Up Task | Rolled Up Milestone | External Tasks

DELAWARE COUNTY ROAD IMPROVEMENT PROGRAM - 2009

ID	Task Name	Material	QTY	Duration	Start	Finish	Predecessors
57	North & South Galena		360 TN	1 day	Mon 7/13/09	Mon 7/13/09	32
58	North Old State		2213 TN	2 days	Fri 7/24/09	Mon 7/27/09	33
59	Worthington		113 TN	1 day	Thu 8/13/09	Thu 8/13/09	39
60	Lane		779 TN	1 day	Mon 8/31/09	Mon 8/31/09	43
61							
62	**Chip Seal - Small's Asphalt Paving**		**632,404 SY**	**69 days**	**Thu 5/28/09**	**Tue 9/1/09**	
63	Ostrander		15,517 SY	1 day	Thu 5/28/09	Thu 5/28/09	3
64	Concord		5,950 SY	1 day	Thu 5/28/09	Thu 5/28/09	63SS
65	Steitz		15,417 SY	1 day	Thu 5/28/09	Thu 5/28/09	64SS
66	Cook (Crack Seal?)		16,711 SY	1 day	Tue 6/2/09	Tue 6/2/09	
67	Delaware Twp (Law) - Double Chip Seal		3,313 SY	1 day	Tue 6/2/09	Tue 6/2/09	66SS
68	Scioto Twp (Calhoun/Stover/Newhouse/Degood/Slocum)		95,363 SY	2 days	Wed 6/3/09	Thu 6/4/09	67
69	Thompson Twp (Fulton Creek/Mooney/Donovan)		64,404 SY	2 days	Fri 6/5/09	Mon 6/8/09	68
70	Troy Twp (Troutman/Clear Run)		8,700 SY	1 day	Tue 6/9/09	Tue 6/9/09	69
71	Brown Twp (McCurdy/Beard)		14,719 SY	1 day	Tue 6/9/09	Tue 6/9/09	70SS
72	North & South Galena		89,733 SY	2 days	Tue 7/7/09	Wed 7/8/09	18
73	North Old State		78,478 SY	2 days	Fri 7/17/09	Mon 7/20/09	20
74	Kingston Twp (Stockwell/Wilson/Blaney/Rosecrans/Wildwood Ln)		50,165 SY	2 days	Tue 7/21/09	Wed 7/22/09	73
75	Harlem Twp (Trenton/Gosuch/Special Items)		38,062 SY	2 days	Thu 7/23/09	Fri 7/24/09	74
76	Porter Twp (Lane)		20,170 SY	1 day	Tue 9/1/09	Tue 9/1/09	
77							
78	**Strawser, Inc.-SAMI (Fiber)**		**8,467 SY**	**4 days**	**Mon 8/3/09**	**Thu 8/6/09**	
79	Orange Twp (Green Bower/Sloop/Payson/Colonial Meadows)		17,360 SY	4 days	Mon 8/3/09	Thu 8/6/09	
80							
81	**Strawser, Inc.-Crack Seal**		**101,602 LBS**	**74 days**	**Tue 5/26/09**	**Fri 9/4/09**	
82	County/Township Wide Crack Sealing		101,602 LBS	74 days	Tue 5/26/09	Fri 9/4/09	
83							
84	**Strawser-Micro-Surfacing**		**203,501 SY**	**8 days**	**Mon 7/27/09**	**Wed 8/5/09**	
85	N. Old State/N.&S. Galena/Cheshire West/Delaware Twp		203,501 SY	8 days	Mon 7/27/09	Wed 8/5/09	
86							
87	**Pavement Technology-Asphalt Rejuvenating Agent**		**85,481 SY**	**3 days**	**Wed 7/1/09**	**Fri 7/3/09**	
88	Sunbury Rd. (Westerville City limits to Sunbury Village limits)		85,481 SY	3 days	Wed 7/1/09	Fri 7/3/09	
89							
90	**Griffin Pavement Striping**			**74 days**	**Tue 5/26/09**	**Fri 9/4/09**	
91	Various County/Township Roads			74 days	Tue 5/26/09	Fri 9/4/09	

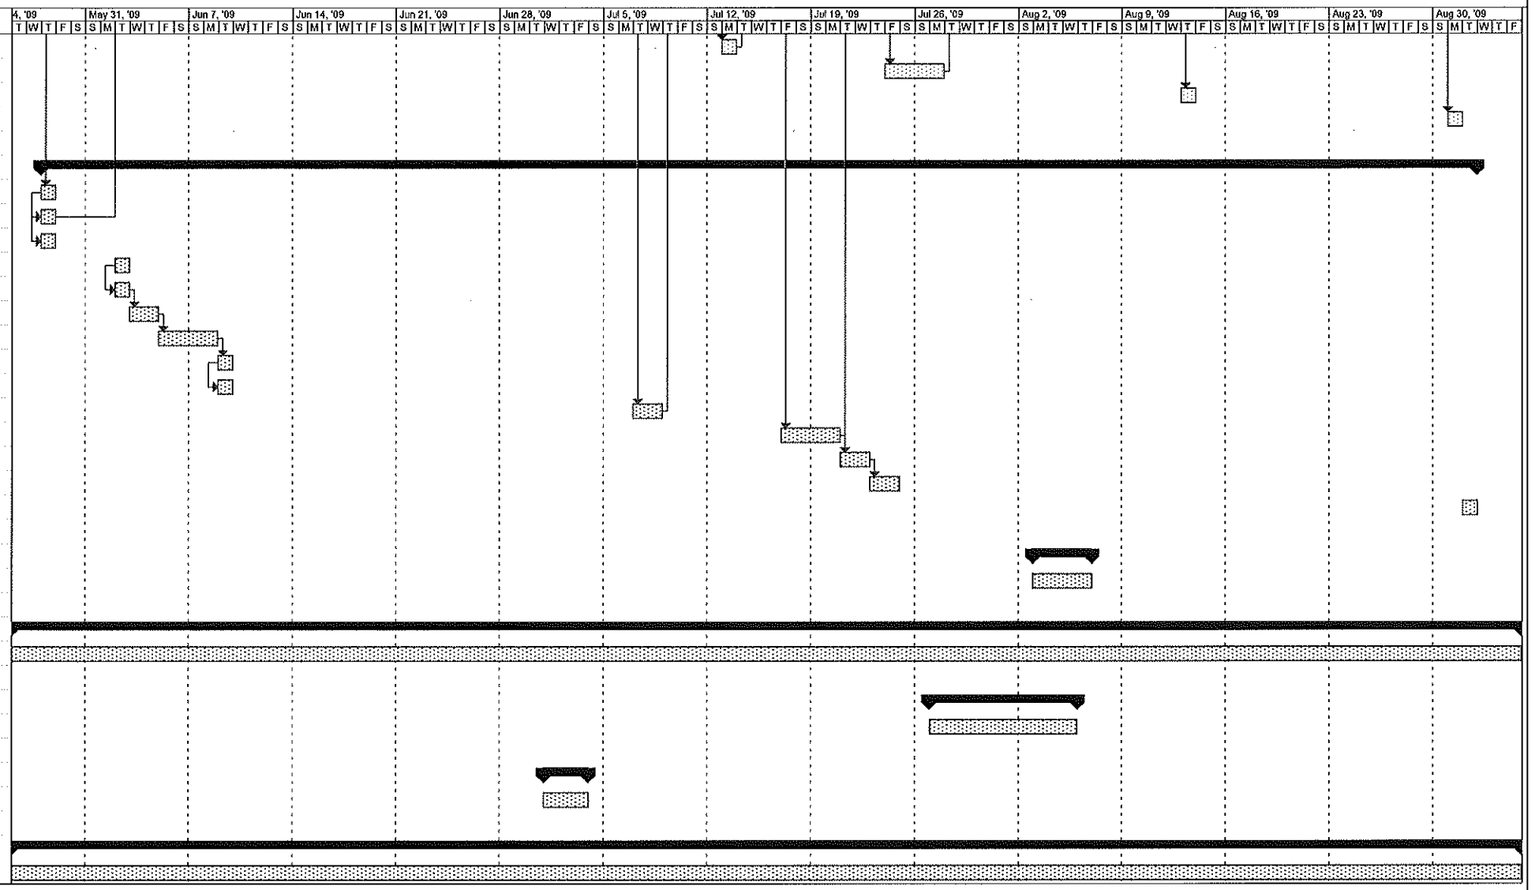

Project: Delaware Co
Date: Wed 5/20/09

Task · Split · Progress · Milestone · Summary · Rolled Up Task · Rolled Up Split · Rolled Up Milestone · Rolled Up Progress · External Tasks · Project Summary
